

**ST. JOSEPH'S A. MCKAY ELEMENTARY SCHOOL  
PROJECT STATUS REPORT  
December 2024**

**New grades PP-6 replacement school project in north end Halifax**


Modern, daylight filled learning environment, maximizing use of existing site  
Integrated childcare centre

General Project Information		Contacts re: concerns or questions	
Project Sponsor Group	NS Dept. of Public Works NS Dept. of Education and Early Childhood Development Halifax Regional Centre for Education	Construction related	John Rhynold, Marco Site Superintendent, During regular business hours at 902-209-4399 or jrhynold@marcogroup.ca
Design Consultant	Stantec Architecture Ltd.	General Project	Muree Ali, DPW Project Manager During regular business hours at 902-717-0599 or muree.ali@novascotia.ca
General Contractor	Marco Group		

Rendering of building exterior



Site Plan

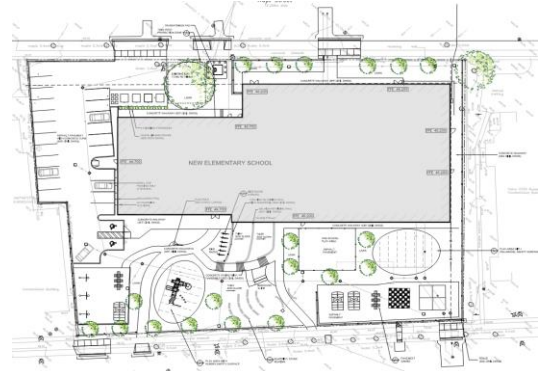

Building Structure - end-November 2024



Interior Works



2024						2025											
SUMMER		2024-25 SCHOOL YEAR						SUMMER		2025-26 SCHOOL YEAR							
J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D
					CURRENT MONTH							Substantial Completion					
MAIN BUILDING						CONSTRUCTION											

**PROJECT STATUS**

- Exterior wall and floor slab installation ongoing.
- Interior partitions installations ongoing.
- Mechanical & electrical installations ongoing.

**SAFETY NOTICE**

This is an active construction site. No persons are allowed on site without appropriate protective equipment as directed by the Marco Group construction signage posted at site entrances.

Marco Group will make every effort to minimize impacts on neighbours and will follow municipal construction guidelines including traffic control, and noise restrictions.
